Wailea Ekahi Pavilion Project Schedule

ID	Task Name	Duration	Start	Finish	Predecessors
1	Mobilization	2 days	Mon 4/29/19	Tue 4/30/19	
2	Dust Fence & Access	5 days	Wed 5/1/19	Tue 5/7/19	1
3	Pool Closure Equipment Re-position	2 days	Wed 5/15/19	Thu 5/16/19	2FS+5 days
4	Plumbing & Electrical Demolition	3 days	Wed 5/8/19	Fri 5/10/19	2
5	Pool Closure for Demo	3 days	Tue 5/7/19	Thu 5/9/19	2FS-1 day
6	Demolition Structure	10 days	Tue 5/7/19	Mon 5/20/19	4FS-4 days
7	Demolition Foundation	10 days	Mon 5/27/19	Fri 6/7/19	6FS+4 days
8	Demolition CMU	7 days	Wed 5/29/19	Thu 6/6/19	3FS+8 days
9	Excavation and Grading	4 days	Mon 6/10/19	Thu 6/13/19	7
10	Footings And Compaction	10 days	Fri 6/14/19	Thu 6/27/19	9
11	Foundation Reinforcement	30 days	Fri 7/5/19	Thu 8/15/19	10FS-2 days
12	Pour Grade Beams and Column Foc	2 days	Fri 8/16/19	Mon 8/19/19	11
13	Moment Frame Anchor Plates	2 days	Thu 8/15/19	Fri 8/16/19	11FS-1 day
14	Plumbing U/G	4 days	Tue 8/20/19	Fri 8/23/19	12
15	Electrical U/G	3 days	Mon 8/26/19	Wed 8/28/19	14
16	CMU Block and Planters	14 days	Tue 8/20/19	Fri 9/6/19	12
17	Concrete Slab Pavilion	9 days	Tue 9/3/19	Fri 9/13/19	16FS-4 days
18	In-fill Concrete and Stairs	10 days	Mon 9/9/19	Fri 9/20/19	16
19	Moment Frame Install	4 days	Tue 8/20/19	Fri 8/23/19	12
20	Wood Framing / Roof Trusses	20 days	Mon 9/16/19	Fri 10/11/19	17
21	Water Tight Roof	2 days	Mon 10/14/19	Tue 10/15/19	20
22	Roofing & Skylights	10 days	Mon 12/16/19	Fri 12/27/19	25
23	Steel Framing	10 days	Wed 10/30/19	Tue 11/12/19	21FS+10 days
24	Plumbing Rough-in	7 days	Wed 11/13/19	Thu 11/21/19	23
25	Electrical Rough-in	9 days	Tue 11/26/19	Fri 12/6/19	26
26	Mechanical Rough	4 days	Tue 11/19/19	Fri 11/22/19	23FS+4 days
27	Exterior Siding &Trim	20 days	Mon 12/9/19	Fri 1/3/20	25
28	Trellis Install	10 days	Mon 12/30/19	Fri 1/10/20	
29	Exterior Plaster	15 days	Mon 12/30/19	Fri 1/17/20	31
30	Insulation	4 days	Thu 12/5/19	Tue 12/10/19	25FS-2 days
31	Drywall Hang & Tape	15 days	Mon 12/9/19	Fri 12/27/19	
32	Veneer Rock Columns and Planters	10 days	Wed 12/11/19	Tue 12/24/19	30
33	Door Install	7 days	Thu 1/2/20	Fri 1/10/20	31FS-4 days
34	Interior Trim	15 days	Thu 12/26/19	Wed 1/15/20	31FS-2 days
35	Shower and Fencing	15 days	Thu 1/16/20	Wed 2/5/20	34
36	Painting	14 days	Mon 12/30/19	Thu 1/16/20	31
37	Cabinets	12 days	Tue 1/14/20	Wed 1/29/20	36FS-3 days
38	Stone Counter Tops	2 days	Tue 1/28/20	Wed 1/29/20	37FS-2 days
39	Bathroom Tile	10 days	Fri 1/3/20	Thu 1/16/20	36FS-10 days
40	Tile Floors	20 days	Fri 1/10/20	Thu 2/6/20	36FS-5 days
41	Bathroom Partitions	5 days	Fri 1/17/20	Thu 1/23/20	39
42	BBQ Install	5 days	Thu 1/30/20	Wed 2/5/20	37
43	Plumbing Finish	4 days	Thu 1/30/20	Tue 2/4/20	38
44	Pool Equipment Re-install	4 days	Fri 1/17/20	Wed 1/22/20	36
45	Concrete Sills @ Columns	5 days	Mon 1/20/20	Fri 1/24/20	29
46	Electrical Finish	8 days	Thu 1/23/20	Mon 2/3/20	37FS-5 days
47	Bath Accessories & Mirrors	5 days	Fri 1/24/20	Thu 1/30/20	41
48	Mechanical Finish	2 days	Wed 2/5/20	Thu 2/6/20	43
49	Appliance Install	2 days	Tue 2/4/20	Wed 2/5/20	46
50	Final Inspection- C/O	1 day	Thu 2/6/20	Thu 2/6/20	49
51	Final Cleaning	2 days	Thu 2/6/20	Fri 2/7/20	49
52	Remove Dust fence Demobilize	3 days	Mon 2/3/20	Wed 2/5/20	49FS-3 days

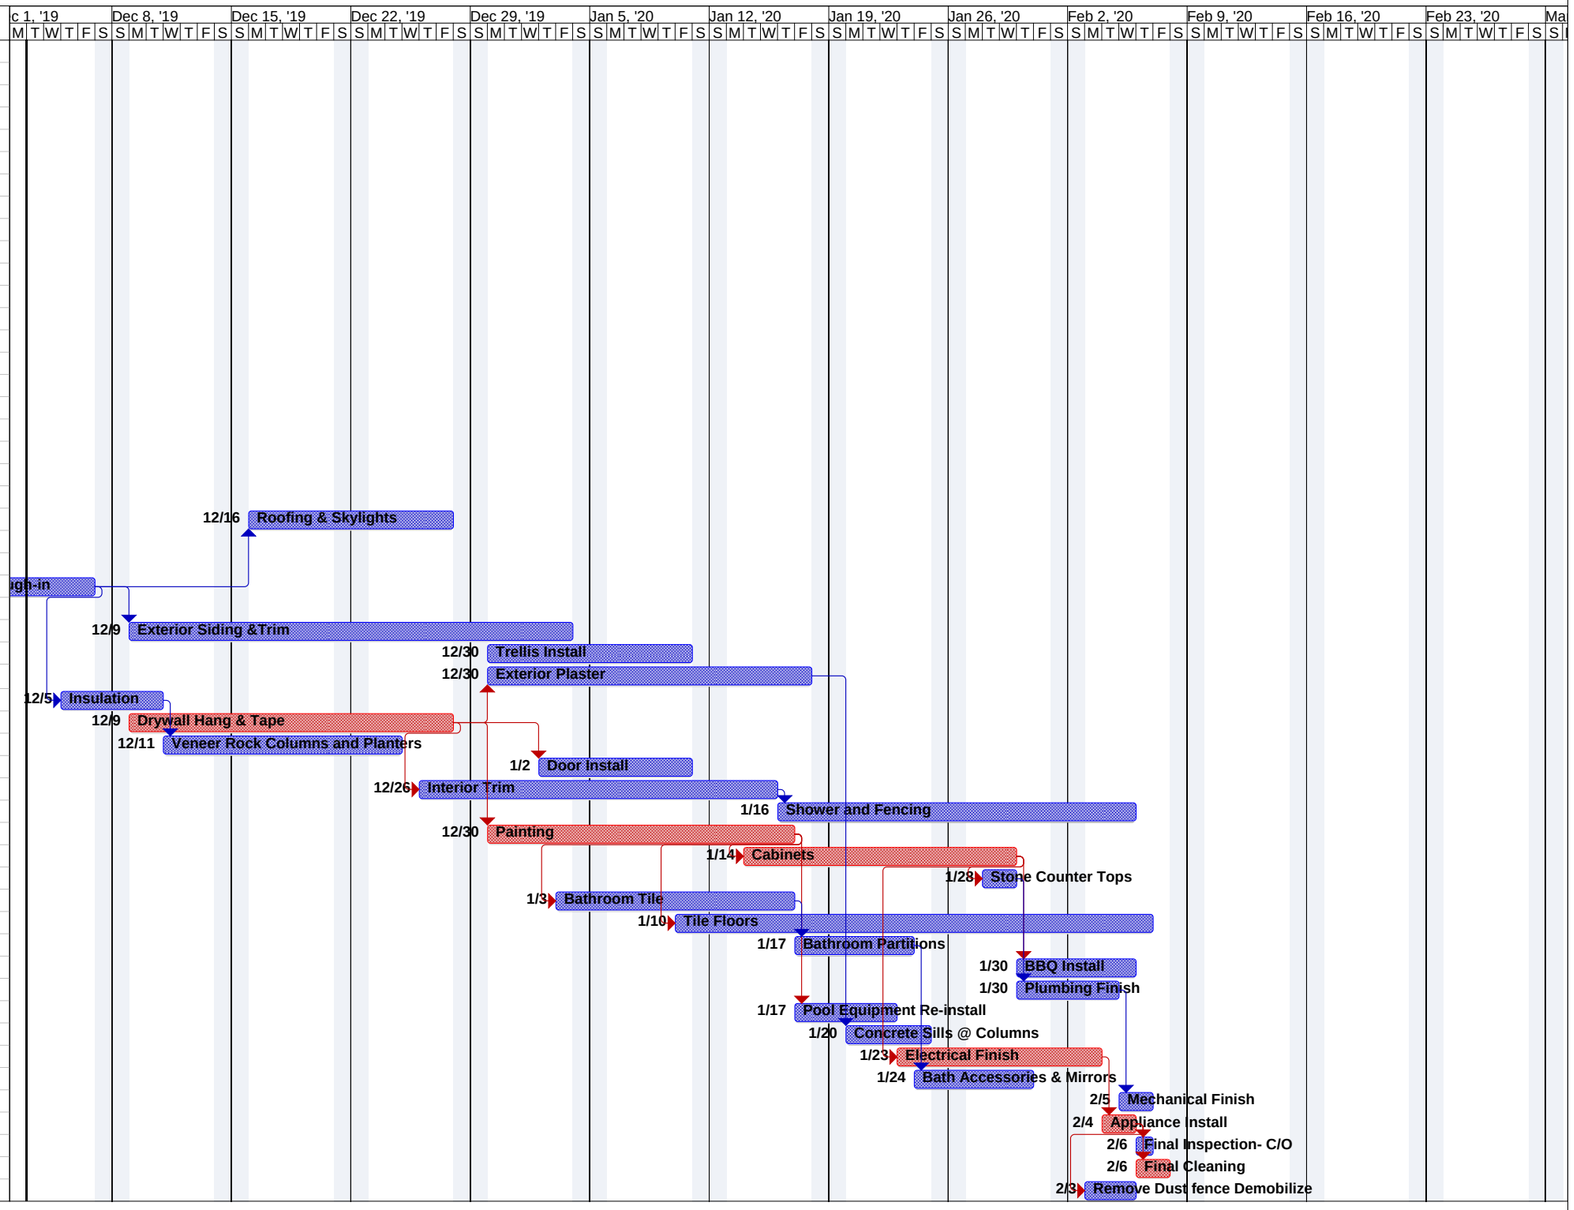

Project: Wailea Ekah Pavilion Project S
Date: Tue 12/3/19

Task	Rolled Up Task	Split	Inactive Task	Duration-only	Finish-only				
Critical Task	Rolled Up Critical Task	External Tasks	Inactive Milestone	Manual Summary Rollup	Progress				
Milestone	Rolled Up Milestone	Project Summary	Inactive Summary	Manual Summary	Deadline				
Summary	Rolled Up Progress	External Milestone	Manual Task	Start-only					
